


Sadkin Center Improvements

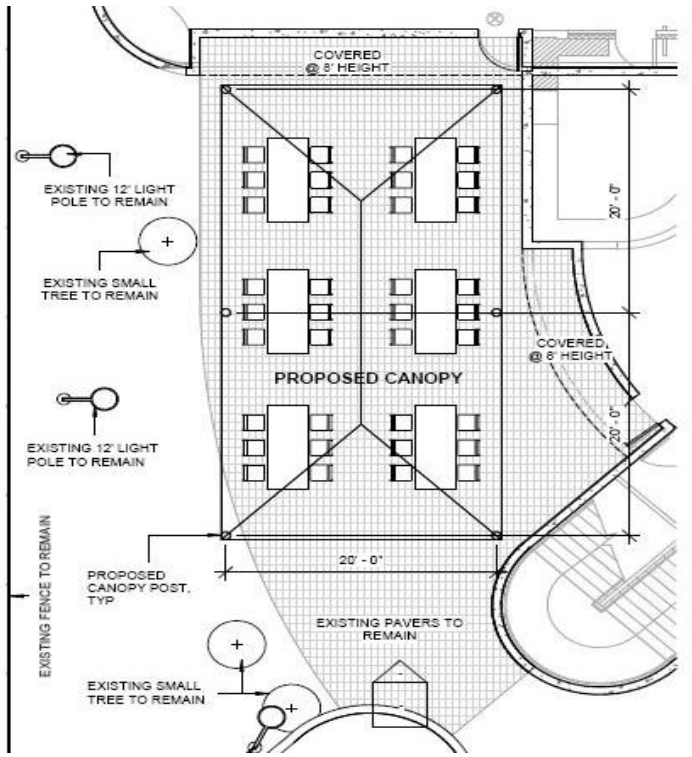

Proposed site plan for new awning on west side of building

Proposed Project Elements:

- New Scoreboards and Bleachers
- New Weight Room Equipment
- New A/C system for building
- New Picnic Tables and Awning for outdoor patio

Milestones

Building Construction Start	December, 2018
Equipment Installation	2019

Project Status:

- Waypoint Contracting has obtained permits, mobilizing for construction
- Gym equipment will be ordered after building renovations complete
- A/C replacement completed in 2017

Project Funding	Budget	Purchase Orders	Expense To Date	Balance
Professional Services	\$52,400	\$4,925	\$43,085	\$4,390
Building/Gym Renovations	541,424	326,504	101,558	113,362
Sports Awning	46,176	0	14,295	31,881
Totals	\$640,000	\$331,429	\$158,938	\$149,633

Current Conditions



A new awning and patio seating area will be added to the exterior of the Sadkin Center

Project Team:

Lead: Brian Picinic, PALS Assistant Director
 Irvin Kiffin, Scott Newton, Vince Miller, Rhea Warner,
 Desorae Giles-Smith

The Sadkin Center basketball gymnasium and grounds will be updated with new air conditioning, park gate, awning and fitness equipment
