

Citywide Median Improvements



Proposed Project Elements:

- Landscaping improvements
- Add and repair irrigation equipment
- Curbing and drainage on Inverrary Boulevard and NW 55 Avenue

Milestones

Median Bids Due	October, 2020
Bid Award	November, 2020
Construction	2021


Project Status:

- Craven Thompson Engineering completing construction plans and front-end bid documents
- Standard design will include integrated pedestrian barriers for safety and maintenance
- Median curb replacement completed by AZR Builders

Current Conditions



Curbing replacement has been completed allowing landscape and irrigation improvements to proceed

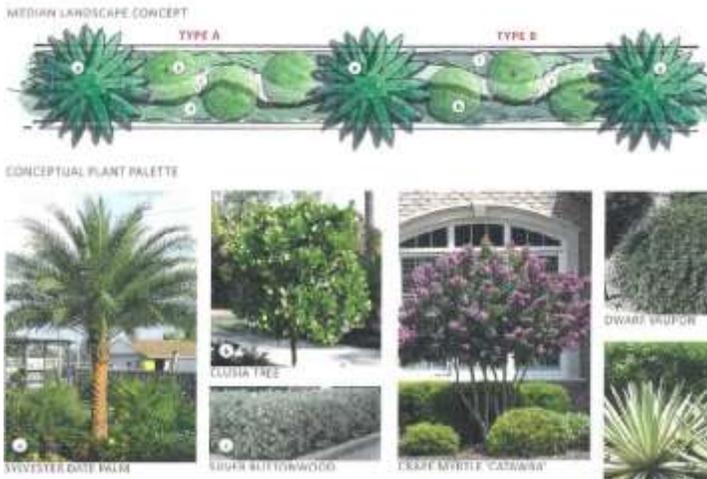

Conceptual plans will be developed for standardized median landscaping throughout Lauderhill

Project Funding	Budget	Purchase	Expense	Balance
		Orders	To Date	
Professional Services	\$97,321	\$19,065	\$78,256	\$0
Median Construction	470,176	0	0	470,176
Curbing Construction	358,160	33,015	325,145	0
Contingency	0	0	0	0
Totals	\$925,657	\$52,080	\$403,401	\$470,176

Project Team:

Leads: Steve Tawes, City Planner

Tamica Dennis, Kennie Hobbs, Jr., J. Martin Cala

City medians have long been a priority in making Lauderhill beautiful. This project will continue that work by adding additional landscaping and renovating older medians.
