

Saint George Park Improvements



Conceptual design for basketball court coverings

Proposed Project Elements:

- Canopy covers for basketball courts
- Playground improvements
- Renovate restrooms
- Walking trail addition
- New sports field and bleachers

Milestones

Design Bid for Fields and Parking Lot	October 2020
Courts/Playground Construction	December, 2020

Project	Purchase Budget	Expense Orders	To Date	Balance
Professional Services	\$307,146	\$15,797	\$203,946	\$87,403
Court Covers	342,244	342,244	0	0
Playground / Walk Trail	136,610	135,485	1,125	0
Restrooms / Building	1,505,909	995,518	256,909	253,482
Field Turf/ Bleachers	528,214	0	7,820	520,394
Totals	\$2,820,123	\$1,489,044	\$469,800	\$861,279

Project Status:

- Building renovations complete May, 2020 but re-opening delayed
- Bid awarded to West Construction for Courts and Playground
- Finance preparing bid for design of parking lot and ballfields
- **See page 2 below for more pictures of building renovations**

Current Conditions



Renovated meeting room at St George Park

Project Team:

Lead: Brian Picinic, PALS Assistant Director
 Irvin Kiffin, Scott Newton, Vince Miller, Rhea Warner,
 Desorae Giles-Smith, Kennie Hobbs, Jr.

The major improvement in St George Park will be canopy covers for the basketball courts, which will protect from sun and rain and allow for more usage by the community.


St George Park Improvements



Before and after renovation pictures of the community meeting room



Before and after renovation pictures of the front desk and lobby area

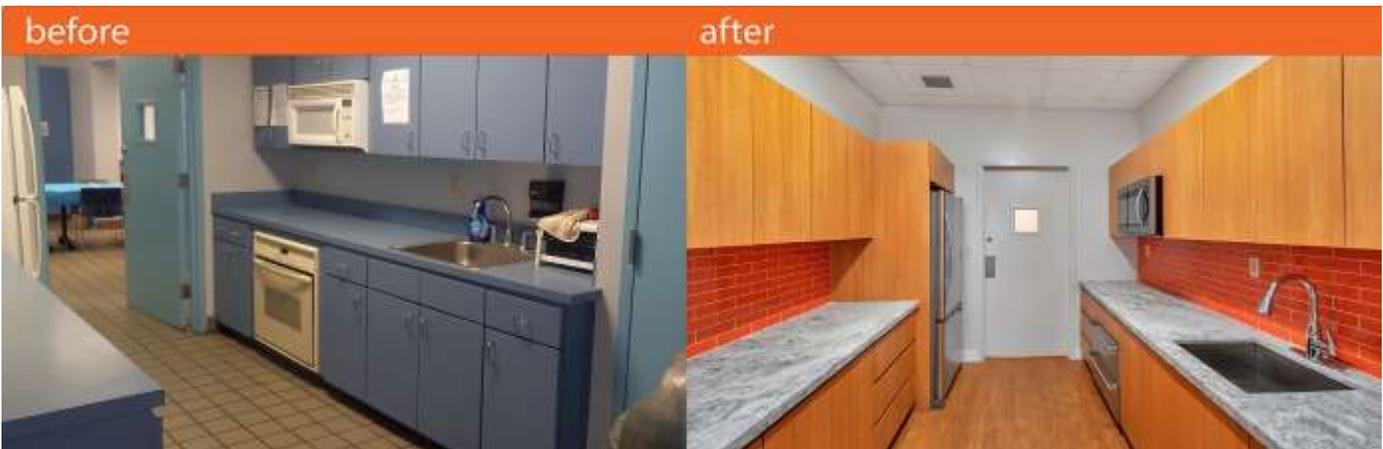

Before and after renovation pictures of the kitchen
