


West Ken Lark Park

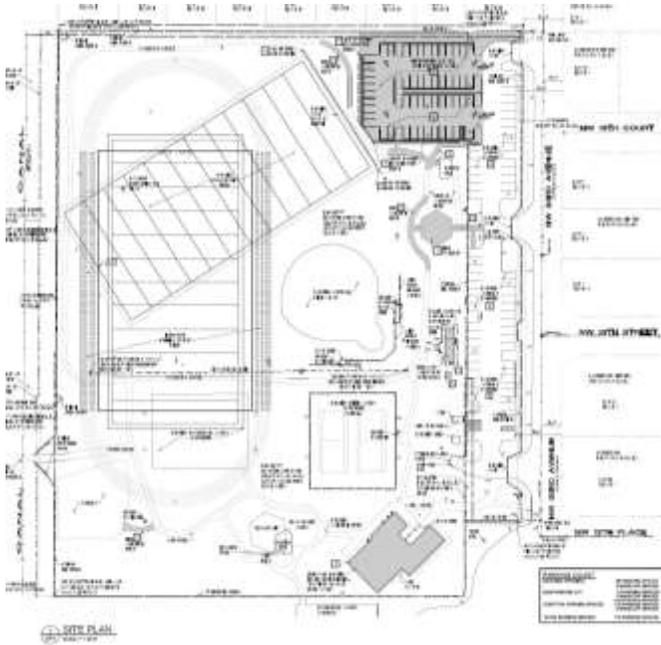

The limited space at West Ken Lark Park will impact the design and location of improvements available

Project	Purchase	Expense		
Funding	Budget	Orders	To Date	Balance
Professional Services	\$80,695	\$18,439	\$62,256	\$ 0
Building	1,009,950	806,635	203,315	0
Pavilion / Playground	85,000	1,054	4,998	78,948
Benches and Bleachers	143,340	122,710	20,630	0
Parking and Walk Path	503,906	503,906	0	0
Totals	\$1,822,891	\$1,452,744	\$291,199	\$78,948

Project Team:

Lead: Brian Picinic, PALS Assistant Director
 Irvin Kiffin, Scott Newton, Vince Miller, Rhea Warner,
 Desorae Giles-Smith, Kennie Hobbs, Jr.

West Ken Lark Park will undergo a total renovation, with improvements to the buildings, pavilions and walking trail and new park signage, benches and bleachers.

Proposed Project Elements:

- Building and Concessions renovation
- Playground, Pavilion, Sign
- Benches and Bleachers
- Parking and Walking Path
- HVAC Replacement

Milestones

DRC Approval	June, 2020
Plans and Permits	August, 2020
Construction	November, 2020

Project Status:

- West Construction providing 100% design
- Project design approved by Development Review Committee
- Started permitting process with Broward County for utilities

Current Conditions



Renovating the buildings and adding to the parking lot at West Ken Lark Park are needed for both existing activities and future plans
